


Westlake				Sulphur Brine Field Containment												25-Jun-25 12:57																																																					
Activity ID		Activity Name		Original Duration	Physical % Complete	Start		Finish		June				July				August				2025 September				October				November				December				2026 January																															
1		08		15		22		29		06		13		20		27		03		10		17		24		31		07		14		21		28		05		12		19		26		02		09		16		23		30		07		14		21		28		04		11		18		25	
📁 Sulphur Brine Field Containment				549d		03-Jun-24 A		30-Dec-25		▼ 30-Dec-25, Sulphur Brine Field Containment																																																											
📁 Milestones				396d		03-Jun-24 A		26-Dec-25		▼ 26-Dec-25, Milestones																																																											
📁 MS1000		Project Start		0d	100%	03-Jun-24 A																																																															
📁 MS1011		Earthen Berm Complete		0d	0%			09-Oct-25		◆ Earthen Berm Complete,																																																											
📁 MS1020		Detailed Design Complete		0d	0%			24-Oct-25		◆ Detailed Design Complete,																																																											
📁 MS1010		Containment - Sulphur Brine Field Complete		0d	0%			26-Dec-25		◆ Containment - Sulphur Brine Field Complete,																																																											
📁 MS1030		Construction Complete		0d	0%			26-Dec-25		◆ Construction Complete,																																																											
📁 Summary				275d		10-Jun-24 A		30-Dec-25		▼ 30-Dec-25, Summary																																																											
📁 General Scope of Work				275d		10-Jun-24 A		30-Dec-25		▼ 30-Dec-25, General Scope of Work																																																											
📁 S0015		Permitting		275d	100%	10-Jun-24 A		30-Dec-25		Permitting																																																											
📁 S0005		Sourcing/Procurement/Contractor Selection		0d	0%			07-Jul-25		◆ Sourcing/Procurement/Contractor Selection,																																																											
📁 S1010		Levees Complete		0d	0%			09-Oct-25		◆ Levees Complete,																																																											
📁 S1020		Detail Design Complete		0d	0%			24-Oct-25		◆ Detail Design Complete,																																																											
📁 S1050		Drainage Control Structures		0d	0%			26-Dec-25		◆ Drainage Control Structures,																																																											
📁 Permitting				276d		10-Jun-24 A		02-Dec-25		▼ 02-Dec-25, Permitting																																																											
📁 P1310		Wetlands Delineation		20d	100%	10-Jun-24 A		02-Jul-24 A																																																													
📁 P1320		Army Corps of Engineers (Emergency Use Authorization Permit)		0d	100%			22-Jul-24 A																																																													
📁 P1490		LDEQ Storm Water Discharge Permit		88d	55%	19-Aug-24 A		07-Jul-25		LDEQ Storm Water Discharge Permit																																																											
📁 P1480		Wetlands Mitigation		43d	0%	01-Oct-25*		02-Dec-25		Wetlands Mitigation																																																											
📁 P1485		Receive Permit		0d	0%			02-Dec-25		◆ Receive Permit,																																																											
📁 Detailed Design				251d		12-Jul-24 A		24-Oct-25		▼ 24-Oct-25, Detailed Design																																																											
📁 Detailed Design				135d		15-Jul-24 A		28-Apr-25 A																																																													
📁 E1340		Start Detail Design		0d	100%	15-Jul-24 A																																																															
📁 E1350		Detailed Design on the Well Pad		10d	100%	17-Mar-25 A		31-Mar-25 A																																																													
📁 E1360		Piling Design		10d	100%	15-Apr-25 A		28-Apr-25 A																																																													
📁 Southeast Dome Levee (Area 10)				14d		07-Apr-25 A		25-Apr-25 A		Levee (Area 10)																																																											
📁 E1740		Southeast Dome Levee (Area 10) IFA		10d	100%	07-Apr-25 A		17-Apr-25 A																																																													
📁 E1750		Southeast Dome Levee (Area 10) IFC		6d	100%	14-Apr-25 A		25-Apr-25 A		IFC																																																											
📁 Southeast Dome Levee (Area 9)				16d		05-May-25 A		30-May-25 A		05-May-25 A, Southeast Dome Levee (Area 9)																																																											
📁 E1760		Southwest Dome Levee (Area 9) IFA		10d	100%	05-May-25 A		16-May-25 A		Levee (Area 9) IFA																																																											
📁 E1770		Southwest Dome Levee (Area 9) IFC		6d	100%	19-May-25 A		30-May-25 A		Southwest Dome Levee (Area 9) IFC																																																											
📁 Finger Lakes (Area 8)				21d		26-May-25 A		27-Jun-25		▼ 27-Jun-25, Finger Lakes (Area 8)																																																											
📁 E1680		Finger Lakes (Area 8) IFA		10d	0%	26-May-25 A		18-Jun-25		Finger Lakes (Area 8) IFA																																																											
📁 E1690		Finger Lakes (Area 8) IFC		7d	0%	19-Jun-25		27-Jun-25		Finger Lakes (Area 8) IFC																																																											
📁 East Salt Lake (Area 7)				169d		09-Sep-24 A		30-Jun-25		▼ 30-Jun-25, East Salt Lake (Area 7)																																																											
📁 E1610		East Salt Lake (Area 7) Design Review		28d	100%	09-Sep-24 A		18-Oct-24 A																																																													
📁 E1620		East Salt Lake (Area 7) IFA		10d	0%	04-Jun-25 A		20-Jun-25		East Salt Lake (Area 7) IFA																																																											
📁 E1630		East Salt Lake (Area 7) IFC		6d	0%	23-Jun-25		30-Jun-25		East Salt Lake (Area 7) IFC																																																											
📁 Dome Levee (Area 6)				21d		19-May-25 A		13-Jun-25		▼ 13-Jun-25, Dome Levee (Area 6)																																																											
📁 E1700		Dome Levee (Area 6) IFA		20d	100%	19-May-25 A		29-May-25 A		Dome Levee (Area 6) IFA																																																											
📁 E1710		Dome Levee (Area 6) IFC		11d	0%	02-Jun-25 A		13-Jun-25		Dome Levee (Area 6) IFC																																																											
📁 West Levee (Area 2)				227d		09-Sep-24 A		22-Sep-25		▼ 22-Sep-25, West Levee (Area 2)																																																											
📁 E1640		West Levee (Area 2) Design Review		28d	100%	09-Sep-24 A		18-Oct-24 A																																																													
📁 E1650		West Levee (Area 2) IFA		10d	0%	29-Aug-25*		12-Sep-25		West Levee (Area 2) IFA																																																											
📁 E1660		West Levee (Area 2) IFC		6d	0%	15-Sep-25		22-Sep-25		West Levee (Area 2) IFC																																																											
📁 Southwest Levee Design (Area 3)				251d		09-Sep-24 A		24-Oct-25		▼ 24-Oct-25, Southwest Levee Design (Area 3)																																																											
📁 E1480		Southwest Levee (Area 3) Design Review		28d	100%	09-Sep-24 A		18-Oct-24 A																																																													
Actual Level of Effort Actual Work					Remaining Work Critical Remaining Work					Milestone summary					Page 1 of 3												Sulphur Brine Field Containment Schedule Progress through Data Date: 13-Jun-25																																										

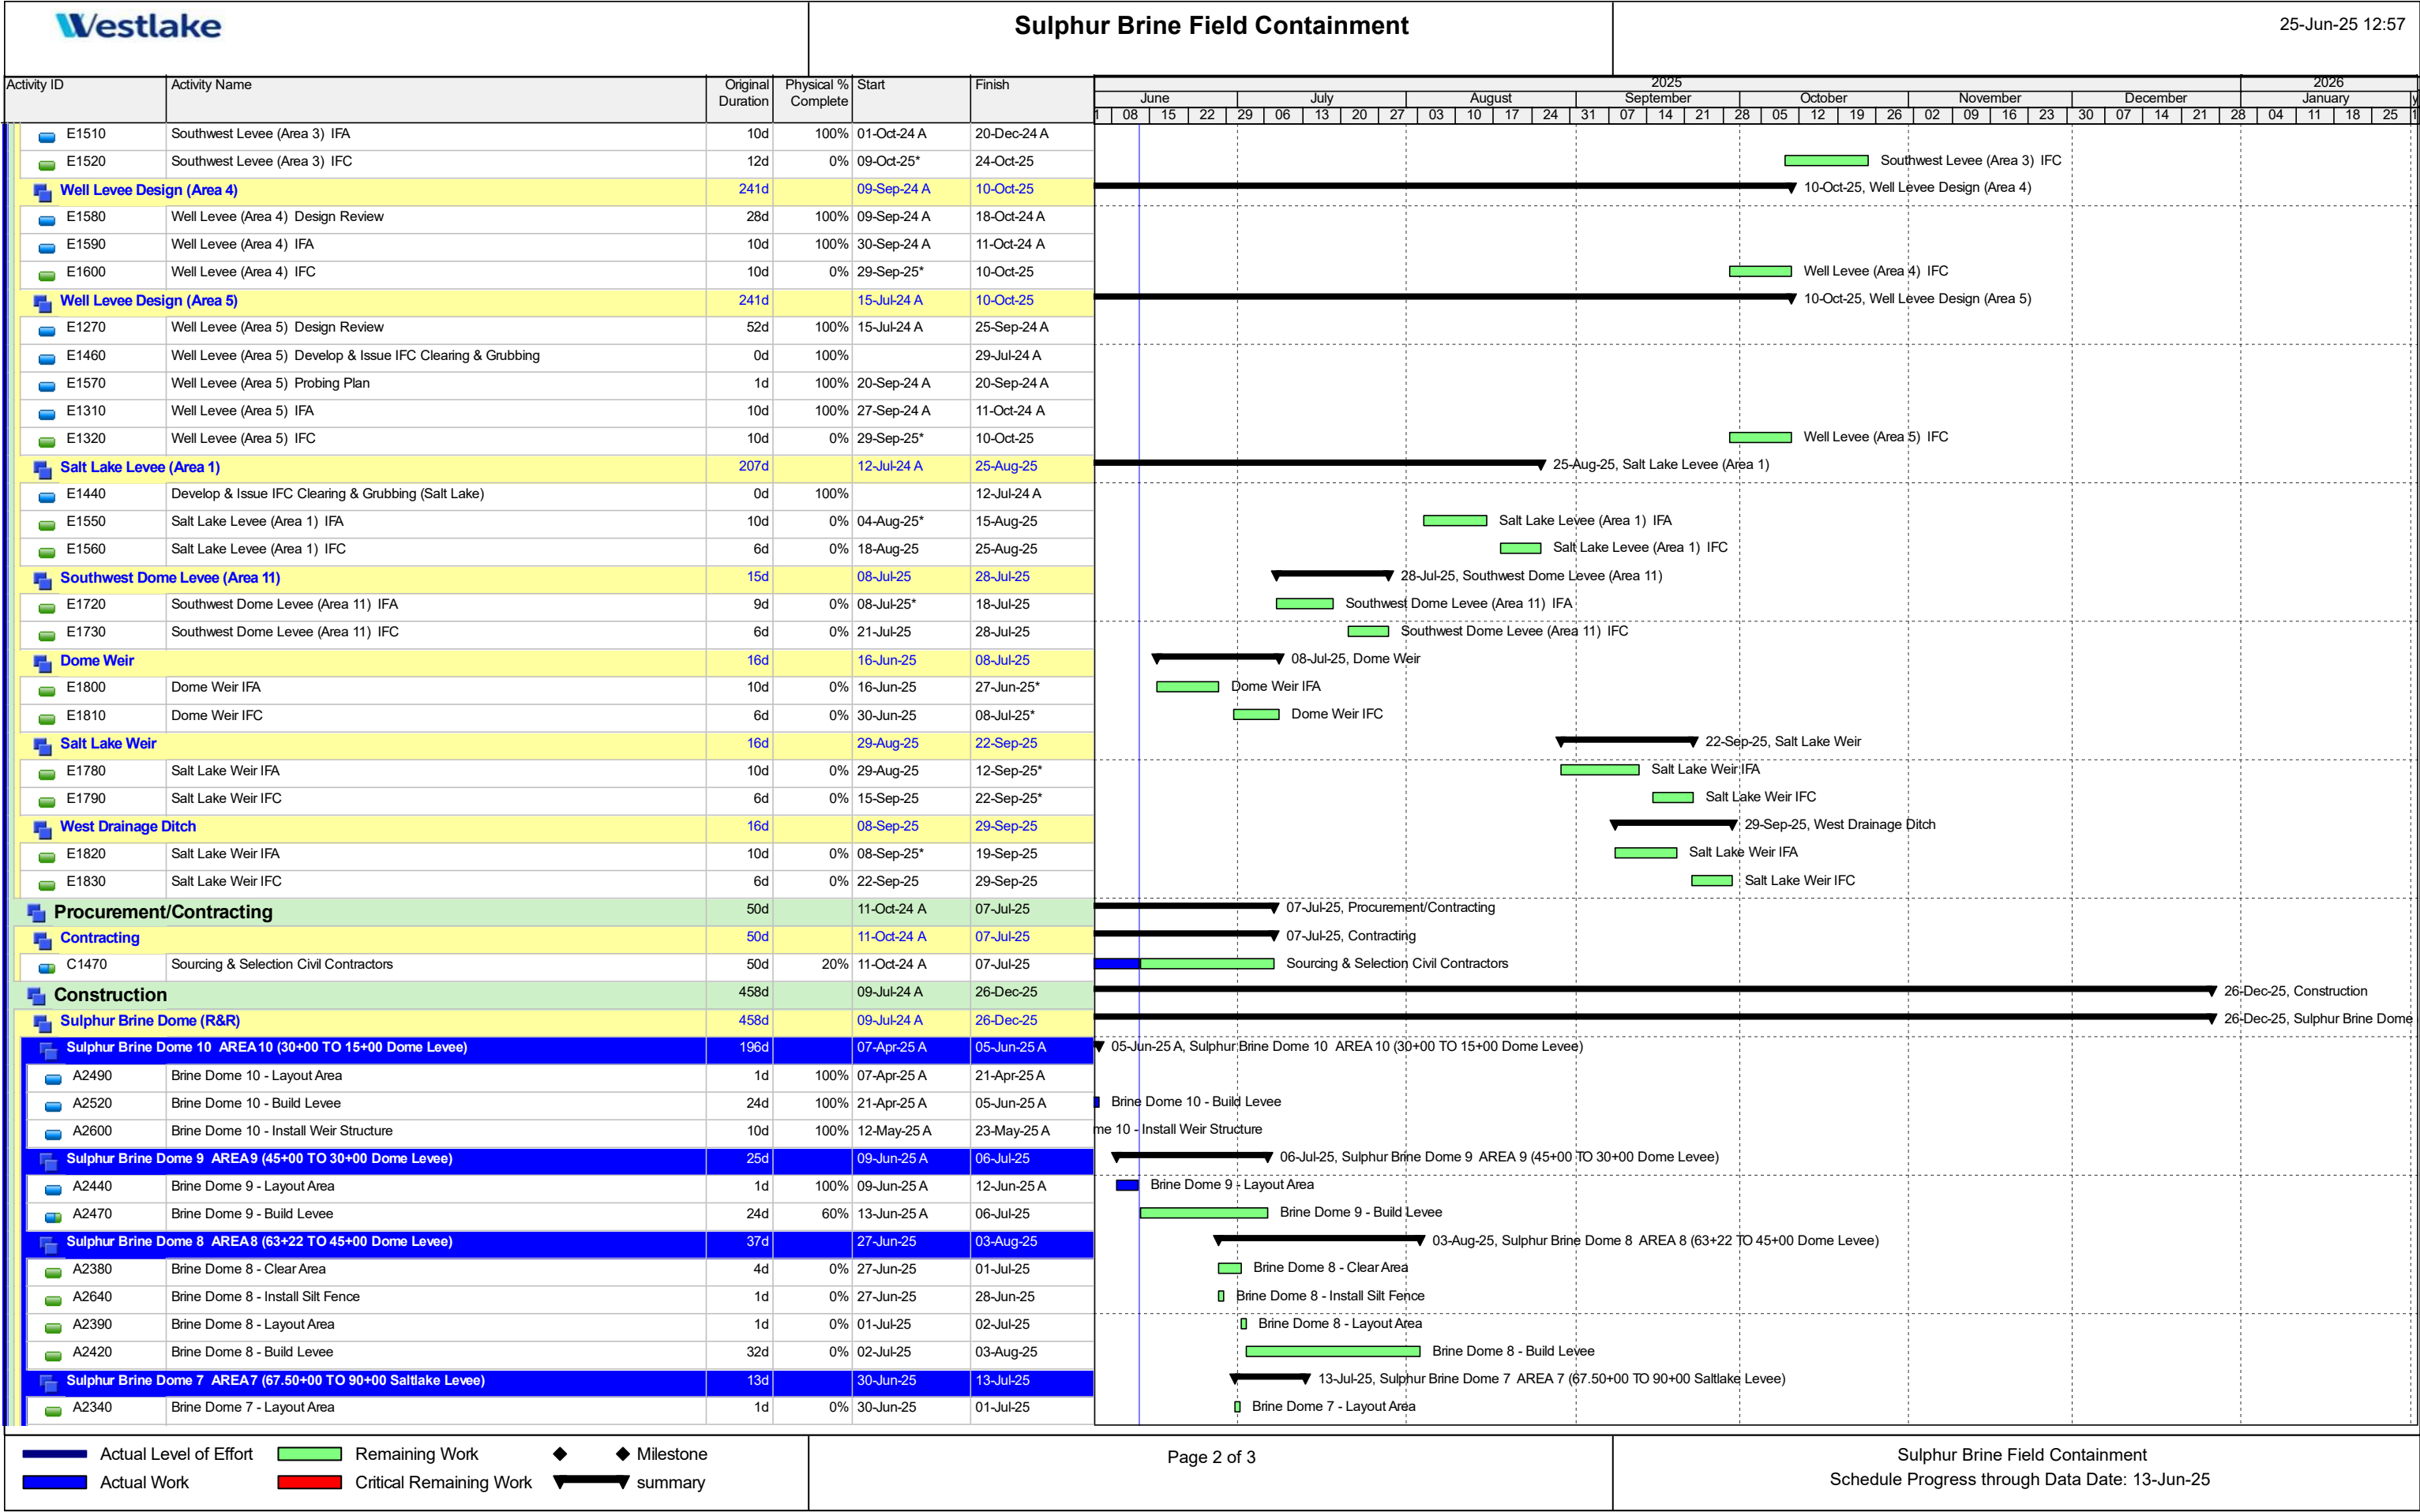

Activity ID	Activity Name	Original Duration	Physical % Complete	Start	Finish	2025																								2026																											
						June				July				August				September				October				November				December				January																							
						1	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25																	
 A2370	Brine Dome 7 - Build Levee	12d	0%	01-Jul-25	13-Jul-25	Brine Dome 7 - Build Levee																																																			
 Sulphur Brine Dome 6 AREA6 (90+00 TO 114+62 Saltlake Levee)		17d		22-Aug-25	08-Sep-25	08-Sep-25, Sulphur Brine Dome 6 AREA 6 (90+00 TO 114+62 Saltlake Levee)																																																			
 A2290	Brine Dome 6 - Layout Area	1d	0%	22-Aug-25	23-Aug-25	Brine Dome 6 - Layout Area																																																			
 A2320	Brine Dome 6 - Build Levee	16d	0%	23-Aug-25	08-Sep-25	Brine Dome 6 - Build Levee																																																			
 Sulphur Brine Dome 11 AREA 11 (15+00 TO 0+00 Dome Levee)		25d		28-Jul-25	22-Aug-25	22-Aug-25, Sulphur Brine Dome 11 AREA 11 (15+00 TO 0+00 Dome Levee)																																																			
 A2540	Brine Dome 11 - Layout Area	1d	0%	28-Jul-25	29-Jul-25	Brine Dome 11 - Layout Area																																																			
 A2570	Brine Dome 11 - Build Levee	24d	0%	29-Jul-25	22-Aug-25	Brine Dome 11 - Build Levee																																																			
 Sulphur Brine Dome 1 AREA1 (0+00 TO 67.50+00 Saltlake Levee)		458d		09-Jul-24 A	13-Jun-25	13-Jun-25, Sulphur Brine Dome 1 AREA 1 (0+00 TO 67.50+00 Saltlake Levee)																																																			
 A2000	Brine Dome 1 - Clear Area	1d	100%	09-Jul-24 A	18-Jul-24 A																																																				
 A2050	Brine Dome 1 - Install Waddle	1d	100%	12-Jul-24 A	22-Jul-24 A																																																				
 A2120	Brine Dome 1 - Rough Grade W/Dozer	6d	100%	04-Oct-24 A	14-Oct-24 A																																																				
 A2010	Brine Dome 1 - Layout Area	1d	100%	14-Oct-24 A	17-Oct-24 A																																																				
 A2040	Brine Dome 1 - Build Levee -Area 1A - EW - South	48d	100%	14-Apr-25 A	25-Apr-25 A	Area 1A - EW - South																																																			
 A2030	Brine Dome 1 - Build Levee -Area 1B - NS	229d	100%	21-Apr-25 A	10-Jun-25 A	Brine Dome 1 - Build Levee -Area 1B - NS																																																			
 A2080	Brine Dome 1 - Build Levee -Area 1C - EW - North	0d	50%	09-Jun-25 A	13-Jun-25	Brine Dome 1 - Build Levee -Area 1C - EW - North																																																			
 Sulphur Brine Dome 2 AREA2 (191+76 TO 167+00 Saltlake Levee)		31d		24-Oct-24 A	22-Nov-24 A																																																				
 A2070	Brine Dome 2 - Clear Trees	3d	100%	24-Oct-24 A	25-Oct-24 A																																																				
 A2060	Brine Dome 2 - Layout Area	1d	100%	24-Oct-24 A	24-Oct-24 A																																																				
 A2090	Brine Dome 2 - Build Levee	31d	100%	25-Oct-24 A	22-Nov-24 A																																																				
 Sulphur Brine Dome 3 AREA3 (167+00 TO TP 135+00 Saltlake Levee)		249d		21-Oct-24 A	26-Jun-25	26-Jun-25, Sulphur Brine Dome 3 AREA 3 (167+00 TO TP 135+00 Saltlake Levee)																																																			
 A2130	Brine Dome 3 - Layout Area	3d	100%	21-Oct-24 A	22-Oct-24 A																																																				
 A2140	Brine Dome 3 - Probe Weir & Pump Station Area	3d	100%	24-Oct-24 A	25-Oct-24 A																																																				
 A2160	Brine Dome 3 - Build Levee	25d	100%	24-Oct-24 A	28-Mar-25 A																																																				
 A2170	Brine Dome 3 -Area 3 Drainage	10d	75%	01-Apr-25 A	26-Jun-25	Brine Dome 3 -Area 3 Drainage																																																			
 Sulphur Brine Dome 4 AREA4 (131+59 TO 135+00 Saltlake Levee)		177d		01-Aug-24 A	11-Jul-25	11-Jul-25, Sulphur Brine Dome 4 AREA 4 (131+59 TO 135+00 Saltlake Levee)																																																			
 A2180	Brine Dome 4 - Clear Area	9d	100%	01-Aug-24 A	09-Aug-24 A																																																				
 A2630	Brine Dome 4 - Install Silt Fence	5d	100%	09-Aug-24 A	14-Aug-24 A																																																				
 A2190	Brine Dome 4 - Layout Area	1d	100%	17-Mar-25 A	17-Mar-25 A																																																				
 A2200	Brine Dome 4 - Probe Area	1d	100%	17-Mar-25 A	17-Mar-25 A																																																				
 A2220	Brine Dome 4 - Build Levee	24d	100%	20-Mar-25 A	16-Apr-25 A																																																				
 Core Well Pad Foundation Piers		20d		13-Jun-25	11-Jul-25	11-Jul-25, Core Well Pad Foundation Piers																																																			
 SL2020	Core Well Pad Foundation Piers	20d	0%	13-Jun-25*	11-Jul-25	Core Well Pad Foundation Piers																																																			
 Sulphur Brine Dome 5 AREA5 (19+23 TO 5+00 Well Levee)		172d		02-Oct-24 A	06-Apr-25 A	TO 5+00 Well Levee)																																																			
 A2250	Brine Dome 5 - Probe Area	13d	100%	02-Oct-24 A	15-Oct-24 A																																																				
 A2230	Brine Dome 5 - Clear Area	1d	100%	04-Oct-24 A	04-Oct-24 A																																																				
 A2240	Brine Dome 5 - Layout Area	3d	100%	04-Oct-24 A	07-Oct-24 A																																																				
 A2260	Brine Dome 5 - Sheet Pile Area	15d	100%	11-Oct-24 A	11-Oct-24 A																																																				
 A2270	Brine Dome 5 - Build Levee	24d	100%	10-Mar-25 A	06-Apr-25 A																																																				
 A2280	Brine Dome 5 - Widen Levee	5d	100%	17-Mar-25 A	21-Mar-25 A																																																				
 Retrofit Drainage Structures		53d		09-Oct-25	26-Dec-25	26-Dec-25, Retrofit Drainage Structures																																																			
 A2670	Area 2 Drainage Structures	20d	0%	09-Oct-25	05-Nov-25	Area 2 Drainage Structures																																																			
 A2710	Area 9 Drainage Structures	20d	0%	06-Nov-25*	05-Dec-25	Area 9 Drainage Structures																																																			
 A2690	Area 4 Drainage Structures	3d	0%	08-Dec-25	10-Dec-25	Area 4 Drainage Structures																																																			
 A2700	Area 5 Drainage Structures	10d	0%	11-Dec-25	26-Dec-25	Area 5 Drainage Structures																																																			
