INCIDENT ACTION PLAN

Be brief and concise with your entries

Location		Location	
Bayou Corne		Bayou	Corne
Sink Hole		Sink	Hole

Control Level Company Supervisory

Operational Period

From 5/21/13

To 5/22/13

1.0 SITUATION

Disease, community, environment

PROMPTS:

Weather, disease trends, Resources, Hazards & safety

REFERENCE:

Maps, weather reports, Sitreps, appreciation, warnings, alerts

CURRENT

Mostly Sunny

PREDICTION

Partly Cloudy. 20% chance of precipitation. High Temperature near 89.

2.0 OBJECTIVES (or MISSION)

PROMPTS: Time & space

REFERENCE:

Appreciation – control options, courses open to disease

CURRENT

Objective 1 - Demonstrating sinkhole containment and determining if additional sinkholes could form.

Objective 2 - Locating and mitigating the risk posed by the presence of shallow gas.

Objective 3 - Confirming the broader stability of the Napoleonville Salt Dome.

Current Actions:

Geophone #1 Well

- TD @ 626 on Monday
- Continue to collect grab samples every 10' in overburden and cap rock from shale shaker

ORW Wells/ROI Wells

- Install pump in 19 and 13
- Install tubing in ORW 33

Tilt Meters

- Install corner posts on west side of sink hole.

CPT Well

- Retool CPT rig with new technology

Containment Berm/Roads/Sinkhole

- Continue directional drilling along Sauce Piquante Lane
- Begin placement of GCL/Geotextile/clay on west berm extension.

Version date: 3 May 2010

Gas Sampling and Analysis Program

- Kick off meeting
- Began gas sampling at all bubble sites; gas and water sampling at all GP-BS wells

Expected Actions (Next 24 Hours):

	-Continue directional drilling along Sauce Piquante LaneContinue drilling Geophone #1 and sampling -Continue placement of GCL/Geotextile/clay on west berm extension -Continue pumping ORWs Sinkhole Activity – Code 1			
3.0 EXECUTION add safety information as appropriate				
GENERAL OUTLINE PROMPTS: Strategies & tactics (current/proposed/alternate) REFERENCE: Appreciation, Control Options	Safety Information: See Attached Safe Work Rules Reference IAP dated 8/9/12 Additional to our Safe Work Rules for this project we are adding the awareness of insects, reptiles and animals. Inspect location for flammability Daily Safety Meetings PPE Required on site: Respirator w/ VOC Cartridge, Gloves for sampling, eye protection, life preservers, hearing protection.			
GROUPINGS	NA			
TASKS Including PR & Media	Same as above			
COORDINATING INSTRUCTIONS PROMPTS: Timings, routes, assembly areas, staging areas	Texas Brine Grand Bayou Facility will be used as staging area.			
4.0 ADMINISTRATION (Logistics support) PROMPTS: Unit names, locations, contact names, phone no's, timings, duties/tasks, routes, suppliers, quantities, status (required, organised,				
SUPPLY WHO, WHAT, WHERE, WHEN of resources not readily available	NA			

=	
GROUND SUPPORT Transport of personnel, traffic mgt, refuelling, mechanical repair/maintenance	NA
COMMUNICATIONS Installation, maintenance, technical advice	Cell Phone & Landline Communications: Kenneth Blanchard – Area Manager – 985- kblanchard@texasbrine.com Scott Borne – Facility Manager – 985- sborne@texasbrine.com Joel Miller, PE – Consultant – 337- internet.com Bruce Martin – Operations/PR – 713- bmartin@texasbrine.com Mark Cartwright – Technical/Engineering – 713- mcartwright@unitedbrine.com Scott Whitelaw – Environmental/Safety – 713- swhitelaw@tum.com
STAGING AREA/ FCP Setting up, communications, staffing	Texas Brine Grand Bayou Facility 1301 Hwy 70 South, Belle Rose, La 70341
	ION (Logistics services) s, contact names, phone no's, timings, duties/tasks, routes, suppliers, quantities, status (required, organised,
stand by, enroute)	T
FACILITIES Security, waste, cleaning	NA
CATERING	NA
OH&S/MEDICAL Medical plan, first aid plan	Call 911
FINANCE	NA
TRAVEL	NA
INDUCTION/ TRAINING	NA
ACCOMMODATION	NA

Version date: 3 May 2010

6.0 CONTROL, COORDINATION & COMMUNICATION				
CONTROL & COORDINATION STRUCTURE REFERENCE Structural Chart	Plant Management Supervision / Contractor Work			
COORDINATION & LIAISON Local knowledge, police, agency reps, emergency mgt reps	NA			
COMMUNICATIONS PROMPTS Communications structure, operational comms plan, information mgt	Plant Management – Contractor Communication via Cell Phone			

EXTRAS				
Attachments PROMPTS:: maps, weather, organisational charts, resources, comms diagram	Current Weather Safe Work Rules			
Plan developers PROMPTS PO, Logs Mgr, Controller	NA			
Approval Controller, Ops Director	TBC Company Rep: William Booher FOSC: SOSC: POSC:			

Belle Rose, Louisiana, United States

Today's Forecast: Tuesday, 21 May 2013

89°F


73°F

Sky Conditions: Partly Cloudy Sunrise: 6:07 AM Sunset: 7:54 PM Wind: SSE (163°) @ 13Mph Precipitation Probability: 20%



View your complete Local Weather »

Extended Forecast Full 10-Day Forecast »



Detailed Forecast

Today:

Partly cloudy skies. High 89F. Winds SSE at 10 to 20 mph.

Tonight:

Clear to partly cloudy. Low 73F. Winds SSE at 10 to 15 mph.

Tomorrow:

Partly cloudy with isolated thunderstorms possible. High around 85F. Winds SSW at 5 to 10 mph. Chance of rain 30%.



May 20, 2013

Mr. Bruce Martin Vice President of Operations Texas Brine Company, LLC 4800 San Felipe Houston, TX 77056

Dear Mr. Martin:

RE: In-Place Inclinometer, Tiltmeter, and Water-Level Monitoring System, Napoleonville Dome Weekly Report: May 11, 2013, Through May 17, 2013

RESPEC is pleased to submit this weekly report on the in-place inclinometer (IPI), tiltmeter, and water-level monitoring system installed around the sinkhole located near the western flank of the Napoleonville Dome, Assumption Parish, Louisiana. Water-level data in this report and the attached Excel file are submitted in response to Directive #5 contained in the October 11, 2012, Third Amendment to Declaration of Emergency and Directive from the Department of Natural Resources Office of Conservation. IPI and tiltmeter data are also attached as Excel files.

Monitoring locations are illustrated in Figure 1, and graphs that illustrate the tilt data, as recorded by each instrument, are provided in Figures 2 through 4. The IPI data for the X-directions and Y-directions are plotted separately in Figures 2 and 3, respectively. The tiltmeter data for both the X- and Y-directions are plotted in Figure 4. A condition reflecting no changes in ground movement plots as a horizontal line on these graphs. Note that the instruments installed are very sensitive; they can measure ground tilt to less than 1/1,000 of a degree. Inclinometer alarm levels are set at ± 1.0 degree, and tiltmeter alarms are set at ± 0.5 degree.

This week, tilt readings from inclinometer IPI-3a indicate a fairly steady 0.14 degree movement toward the south. IPI-4 and IPI-5 became submerged, and communication with the instruments was lost at 13:00 on May 10 because of a breach in the western berm after a heavy rainstorm. Instruments are still below water level and cannot be safely retrieved until water levels decrease.

Figure 5 shows water-level temporal trends at the IPI-2 and Rig Access Road transducers. Figure 6 shows water-level temporal trends at the Pad 3 and Rig Access Road transducers. Water levels inside the berm slowly increased through May 12 and have been slowly dropping since.

Sincerely.

Eric L. Krantz Engineer

ELK:llf

Enclosure

cc: Mr. Mark Cartwright, Texas Brine Company, LLC Mr. Scott Borne, Texas Brine Company, LLC Project Central File 2153 — Category C

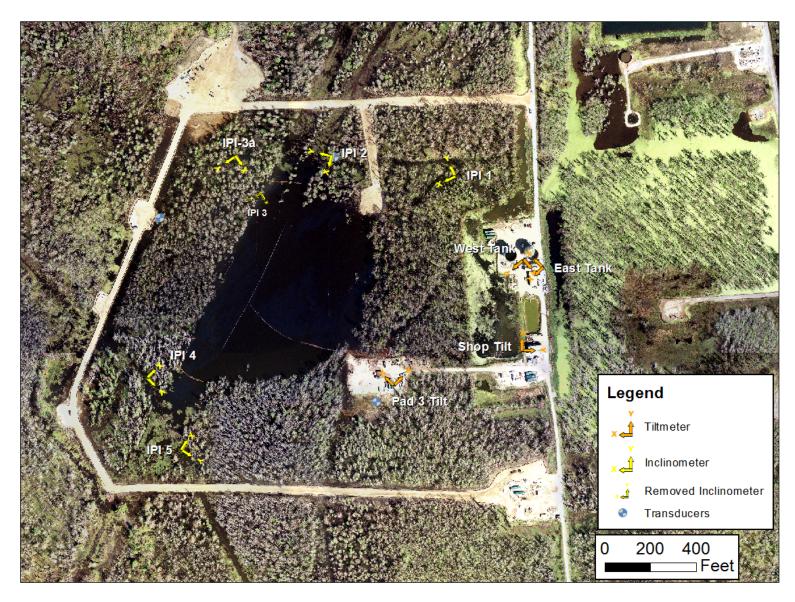


Figure 1. Monitoring Locations.

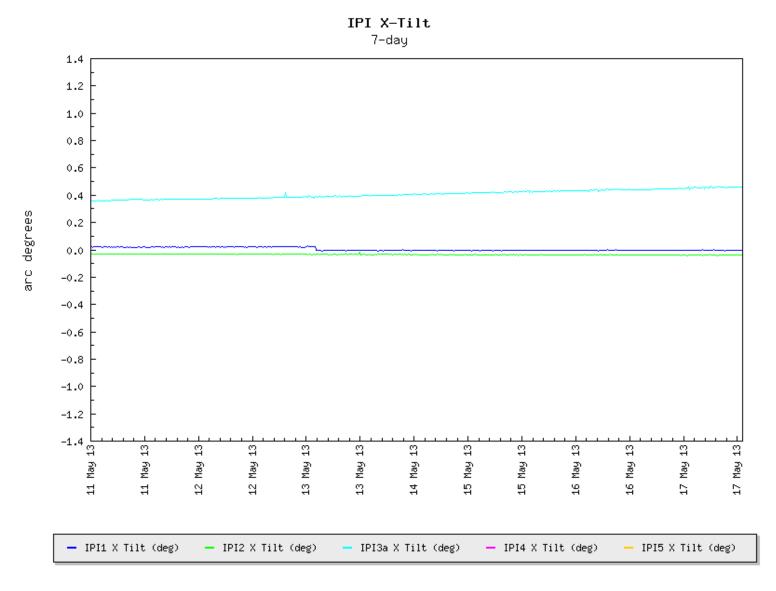


Figure 2. Inclinometer *X*-Direction Temporal Trends.


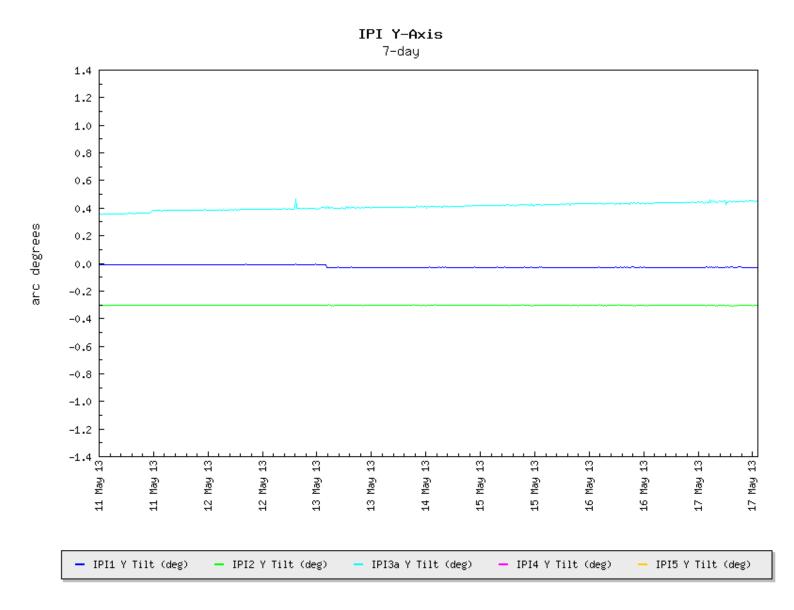


Figure 3. Inclinometer *Y*-Direction Temporal Trends.

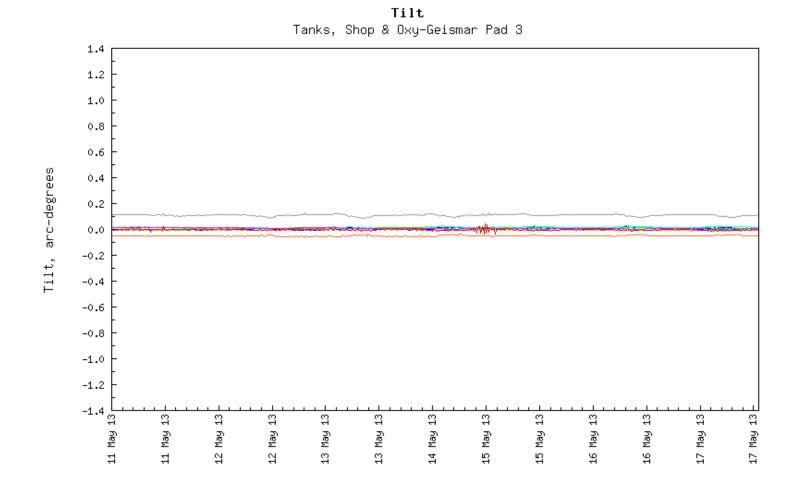

Tanks-West X

Tanks-East X

— Pad 3 X

- Tanks-East Y


— Pad 3 Y

Figure 4. Tiltmeter Temporal Trends.

Tanks-West Y

Shop X

- Shop Y

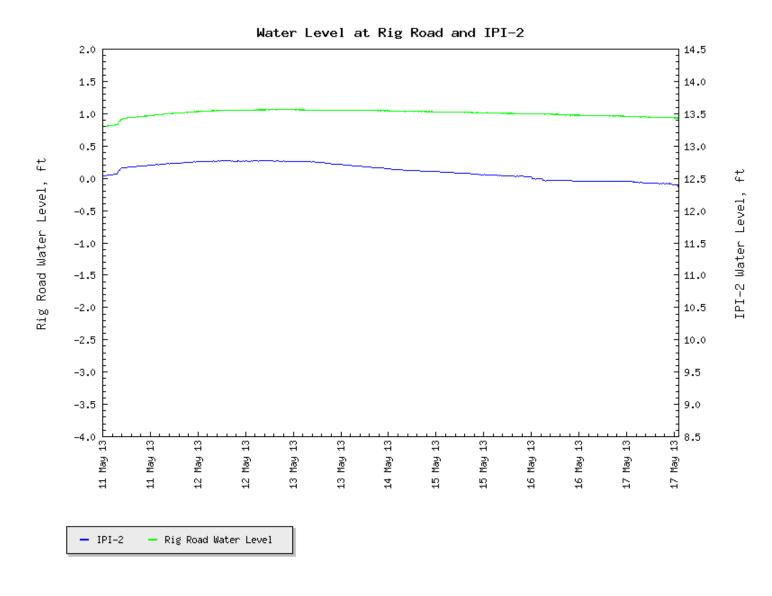

 $\textbf{Figure 5.} \ \ \text{Water-Level Temporal Trends Showing Rig Access Road Data and IPI-2 Data}.$

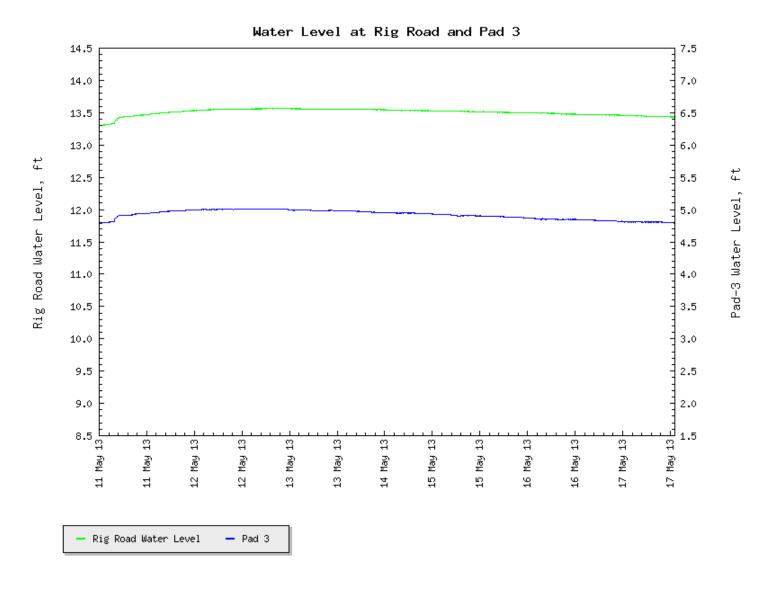


Figure 6. Water-Level Temporal Trends Showing Rig Access Road Data and Pad 3 Data.

Site Specific Safety Plan for Remediation of the Bayou Corne Sink Hole

The following plan is a site specific plan for the remediation of the Bayou Corne sink hole which will be achieved in two Phases. Phase one will include the construction of an access road to the sink hole which will allow the use of a long reach excavator. The excavator will be used to remove vegetation near the access road and place into roll off boxes. Phase two will consist of placing one or more airboats with attached rakes that will be used to push vegetation towards the access road where it will be removed and placed in roll off boxes. By removing the vegetation this allow us the use of skimmers and absorbent booms to aid in hydrocarbon removal.

Site Setting

The Texas Brine facility is located at 1301 Hwy 70, Belle Rose, LA 70341. The facility is located South of 70. The site is located on raised pads and roads but the property is otherwise swamp. A site map is attached. The nearest hospital, Our Lady of the Lake is located in Napoleonville, LA. which is a 15 minute trip.

Site Specific Hazards

The site is located in a swamp setting and potential dangers may be present. Personnel should be aware of:

Alligators

Wasps

Snakes

Spiders

Emergency Contact

911 will used in any emergency. Cell phones on site

Site Safety

Safety Meeting

Held at the beginning of each shift.

PPE Requirements

Hard hat

Safety Glasses

Steel toe boots

Air Monitoring

A system of air monitoring devices have been placed across the property surrounding the sink hole. One air monitoring device is located next to the access road.

Airboats will have hand held monitors on there person at all times when on the sink hole.

Spotters and Warnings

A person or persons armed with an air horn will be placed on site looking for safety issues such as:

Leaning trees

Falling trees

Ground Movement

Driver of the truck attached to the roll off box will remain in the truck at all times and will be ready to vacate the access road on signal.

Heavy Equipment

Long reach excavator

Environmental

Vegetation will be placed in lined roll off boxes and disposed of.

Airboats will remain inside the containment boom once entered.

Decon of airboats will take place on location pad next to access road.

TBC Oxy Grand Bayou Sinkhole Management Plan

Phase Two- Crude Oil/Vegetation/Debris Removal

10-12-2012

(THIS PLAN CAN BE ADJUSTED BY TBC FOR WEATHER RELATED ISSUES, OR SITE CONDITIONS)

This plan is being followed as an approach to sinkhole management. The primary focus for this plan is to:

- Recover liquid hydrocarbons that are found on the surface of the sinkhole. By removing the free
 phase Hydrocarbons that are found on the surface of the sinkhole, off-site migration of these
 Hydrocarbons will be greatly reduced. Thus, limiting the impacts of the Hydrocarbons to the
 sinkhole surface and the immediate area. Additionally, the removal of the free phase
 Hydrocarbons will greatly reduce the "smell" associated with the sinkhole.
- 2. To further understand the dynamics of the sinkhole, through profiling and visual observation of the surface of the sinkhole.

Phase One focused on the removal of floating vegetation and debris within the sinkhole. To date, the vast majority of floating vegetation and debris has been cleaned and cleared off of the surface of the sinkhole area. On October 8, 2012, we began to bring on site equipment and staffing to move into Phase Two of the Sinkhole Management, Crude Oil Removal.

Crude Oil removal will take place on near the mat road that was constructed on September 24, 2012. Texas Brine began reconstruction of the mat road at well pad #3, going toward the sinkhole. This road has been constructed of river sand, filter fabric and wooden mats. The mat road has been constructed in the previous footprint, to the outside and on the eastern side of the sinkhole.

As discussed in the Phase One Plan for Sinkhole Management, the mat road will play a vital part in our recovery of oiled vegetation and crude oil removal. Texas Brine plans to collect crude oil via physical means with skimmers, and vacuums. We will also use Air Boats to sweep the surface of the sinkhole. Texas Brine has fabricated an oil collection box that will be placed at the end of the mat road, in the water, that will assist in the collection of crude oil.

Product that is recovered will be placed into a frac tank and stored for disposal. These Frac tanks are stored near the sinkhole in an orderly fashion. The vacuum trucks that are used are inspected for leaks and drips prior to leaving the facility for disposal. Occasionally, the Long-reach boom and operator may have to go back out on the mat road to sweep in additional debris that has been swept in by the air boats. The additional debris will be handled as discussed in Phase One. As a safety precaution, the truck driver will be instructed to remain in his vehicle with on ready should any movement be observed on the sinkhole. The truck driver will remain at/in his vehicle during the loading process. A spotter will be placed in a stationary location on Well Pad # 3 to watch for any movement of trees or debris in the sinkhole. Additionally, there will be supervision of the project entire project by TBC Employees.

Texas Brine is following the advice offered by LA DNR and pursuing the use of Oil Gator, as an in-situ remediation of crude oil in hard to reach places or in marginal places where oil may have escaped the containment boom. Texas Brine will not proceed with the use of this material or other materials until approval has been issued by the lead agency on this incident. The use of any such absorbent material will be used to augment the traditional physical oil removal procedures. The proposed use of Oil Gator will not replace the use of traditional physical oil spill removal.

If any personnel or contractors are allowed onto the sinkhole, then personal air monitoring devises will be used to monitor air quality/exposure while on the siinkhole.

The safe execution of this activity is the goal of TBC. This is why every person entering the property, must wear proper PPE (Hard Hat, Long Pants, Steel Toed Boots, and Safety Glasses).

